
BLACK SHEEP / DORSET

Concrete pad centres & utility positions


Hut body: 7,250 x 2,900 mm | Wheels: 500 mm diameter x 75 mm wide | All dimensions in millimetres

SETTING-OUT DRAFT - CONFIRM BEFORE POURING

01 PLAN - LOOKING DOWN

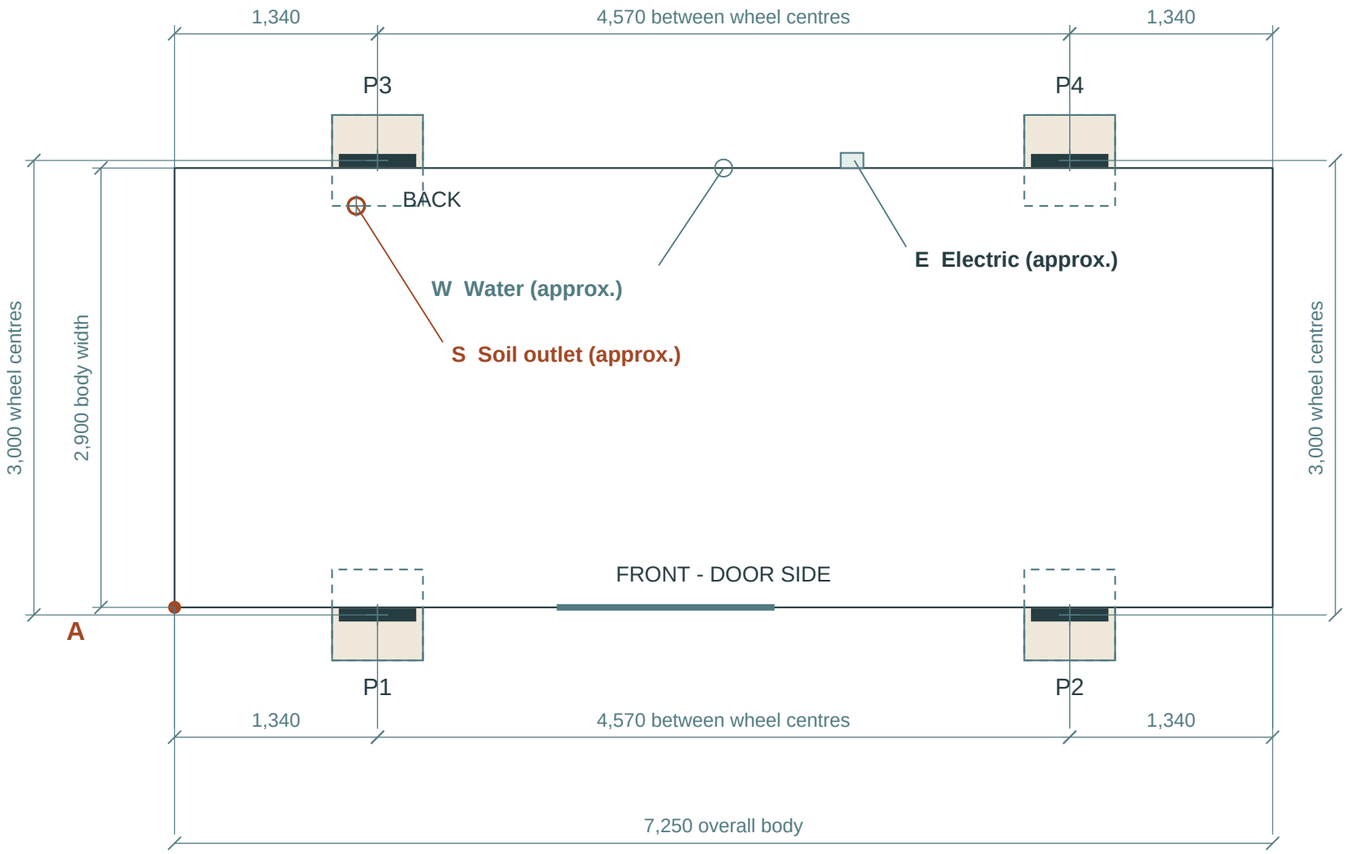


02 BACK ELEVATION

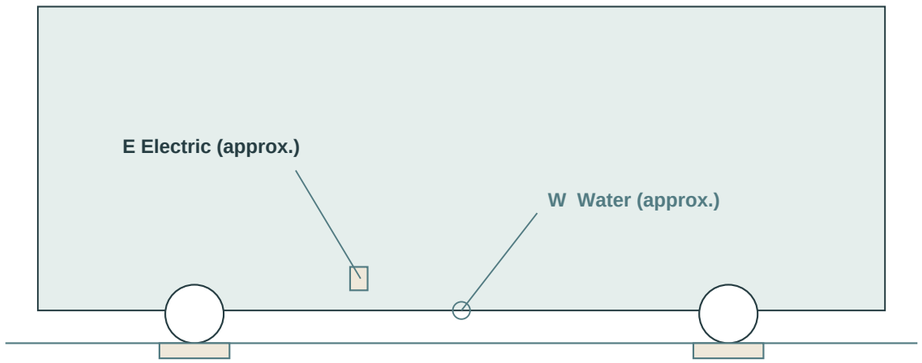

Pad tops: common level | Back view reverses left/right

03 FRONT ELEVATION

Viewed towards the door side; soil outlet shown dashed behind.

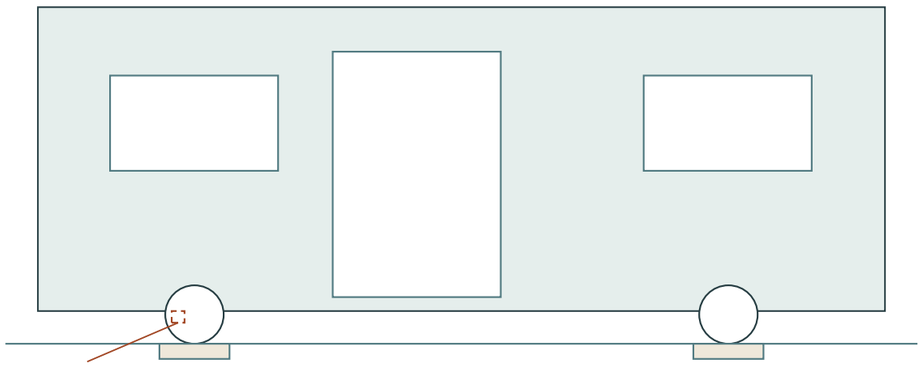

Pad tops: common level

S: soil outlet (approx.)

PAD CENTRE SETTING-OUT SCHEDULE

Measure along the hut from end A. Pads are centred directly beneath each wheel.

Pad	From left body end A	Pad footprint
P1	1,340	600 x 600*
P2	5,910	600 x 600*
P3	1,340	600 x 600*
P4	5,910	600 x 600*

UTILITY POSITIONS - FROM THE SAME BODY EDGES

E: electrical connection on back wall; position indicative only.

S: approx. 1,200 from left body end; approx. 250 in from back wall.

W: water connection approximately midway along the back; confirm on site.

*600 x 600 pads assumed from your earlier brief; confirm size and thickness.

Pad centres: 1,340 from each end; equal 3,000 spacing across at both ends.

Length check: 1,340 + 4,570 + 1,340 = 7,250 mm on both sides.

3,000 across centres retains the 50 mm side allowance; verify on the hut.
